



Portland–Milwaukie Light Rail

TriMet Board Briefing:

Orange Line Opening Status Report



Daniel W Blocher, PE
*Executive Director of
Capital Projects*

January 28, 2015



U.S. Department of Transportation
Federal Transit Administration





PORTLAND-MILWAUKIE

LIGHT RAIL TRANSIT PROJECT



226 08 37 26
DAYS HOURS MINUTES SECONDS

until MAX Orange Line opens

Saturday, September 12, 2015




Rail Activation Readiness

Project Delivery

Operational Readiness

Opening Events



Opening Day
9/12/2015



Project Delivery:

Infrastructure

- West and Bridge Segments are Complete
- East Segment Substantially Complete 2/27
- Systems Installation is ongoing
 - First section from PSU to Clinton Station completed



01/21/2015 09:12

First LRV under power over the Tilikum Crossing



Project Delivery:

Vehicles

- 6 On Site in testing
- 18 Complete by **July 2015**



2014.12.17

Alignment testing of Type V




Project Delivery

- Verification and Testing
 - Construction Safety Certification progress
 - Integrated Testing progress

Over all Safety Certification Summary

1/14/2015

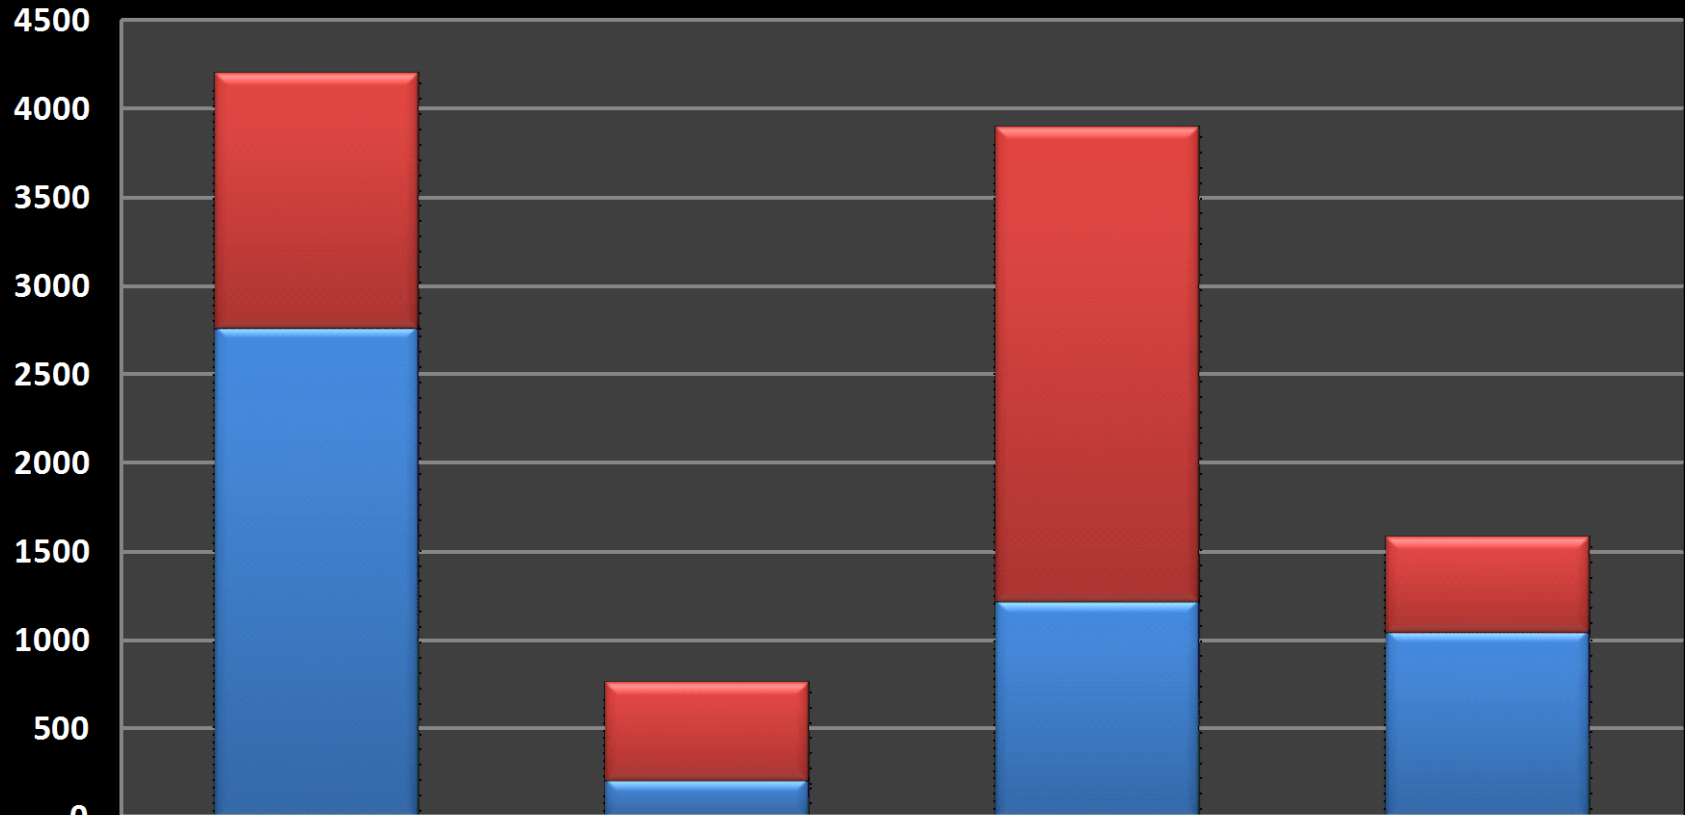

	Civil + Structures	Systems	Vehicles	Others (Ruby, Center, etc)
Remaining	1430	535	2670	533
Complete	2764	217	1218	1047



First LRV at the South Waterfront Station



Operational Readiness

- Numerous Training Plans & SOPs Completed
- Bus Operator training begins March 15th
- Emergency Responder training begins in March
- Rail Operator training begins June 1st



Operational Readiness

- Complete customer information plan
July 1st
- Simulated Revenue Service August 30th
- Service begins September 12th



Opening Events

- Inclusive city wide celebration
- Honor the legacy of transportation development in the region
- Multiple events leading up to opening
- More details to come in coming months

September 12, 2015

